

**CITY OF LOS ANGELES**  
INTERDEPARTMENTAL CORRESPONDENCE

Date: June 1, 2023

To: Street and Transportation Projects Oversight Committee  
Matthew W. Szabo, Office of the City Administrative Officer (CAO), Chair  
Diego de la Garza, Office of the Mayor  
Sharon M. Tso, Office of the Chief Legislative Analyst (CLA)

From: Arsen Voskerchyan, P.E., Division Manager  
Street Improvement Division  
Bureau of Engineering



Subject: **UPDATE OF THE BUREAU OF ENGINEERING STREET IMPROVEMENT PROGRAM MASTER SCHEDULE AND PROJECT STATUS REPORT**

**RECOMMENDATION**

Receive and file the attached updated Street Improvement Program Master Schedule and Project Status Report.

**TRANSMITTALS**

1. Updated Street Improvement Program Master Schedule (Dated May 26, 2023)
2. Updated Project Status Report (Dated May 26, 2023)


**DISCUSSION**

Adjustments have been made to the Street Improvement Program Master Schedule and Project Status Report to reflect updates and changes since the previous submissions.

If you have questions or require additional information, please contact me at Arsen.Voskerchyan@lacity.org.

AV/av

cc: David Hirano, City Administrative Office  
Maria Souza-Rountree, City Legislative Office  
Kevin Minne, Bureau of Engineering

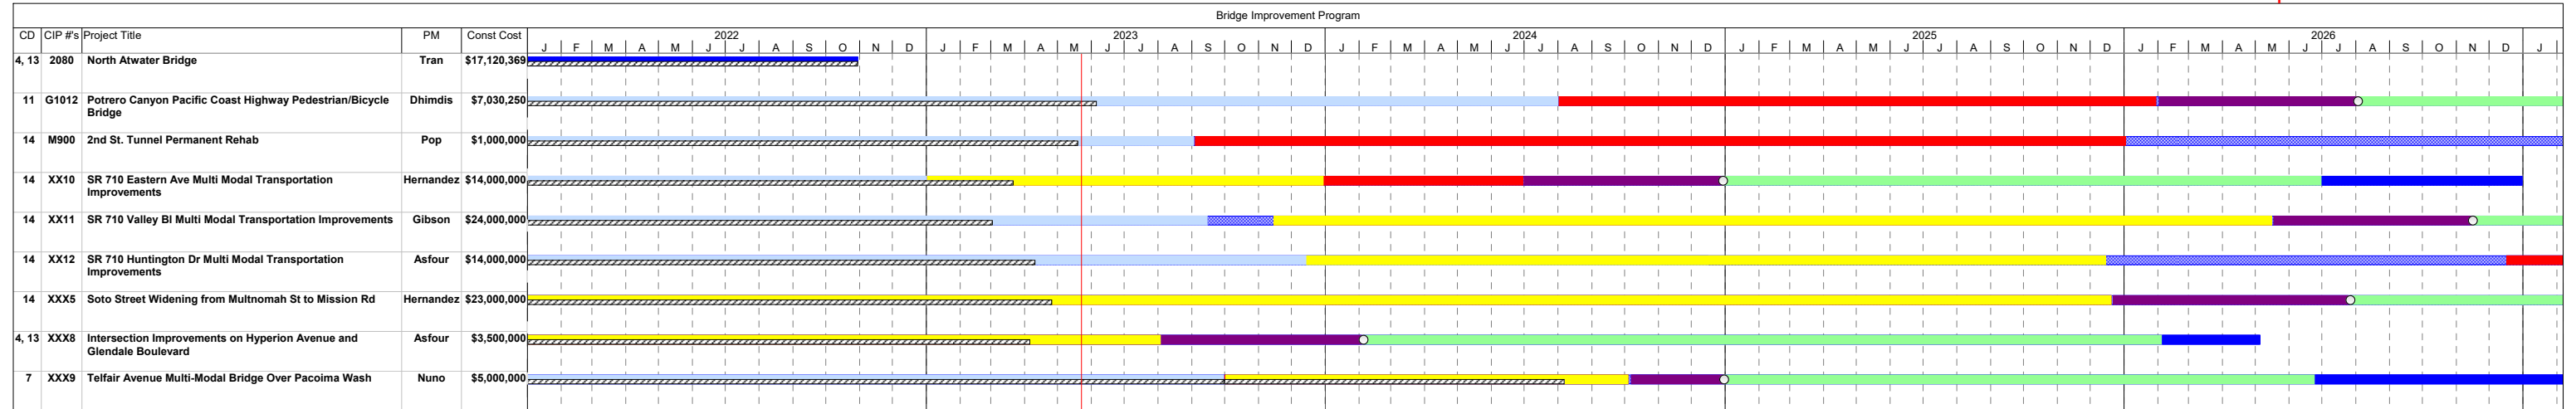

Project: Master Schedule (UPRS)  
Date: Tue 5/23/23

Task	PreDesign	Cons	External Milestone	Inactive Milestone	Manual Task	Manual Summary	External Tasks	External Milestone
Split	Design	PostCons	Deadline	Inactive Milestone	Duration-only	Start-only	External Milestone	External Milestone
Milestone	BidAward	RightOfWay	Inactive Task	Inactive Summary	Manual Summary Rollup	Finish-only	Progress	External Milestone

CD	CIP #s	Project Title	PM	Construction Vehicle	Const Cost	Street Improvement																								
						2022					2023					2024														
						J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	
1	M1008	Kinney Street Improvements Phase 1 - Crestmoore Pl to Knuckle	Medina	Contractor (Regular Award)	\$6,658,000	[Gantt bar for M1008]																								
1	M1024	AHSC Round 3 - Eiden Elms STI & TRA Improvements	Chen	Contractor (Regular Award)	\$3,800,893	[Gantt bar for M1024]																								
1	M1066	ATP 4: Liechty Middle and Neighborhood Elementary Schools Safety Improvement Project	Abbound	Contractor (Regular Award)	\$18,157,000	[Gantt bar for M1066]																								
1	M1099	VALENCIA TRIANGLE LANDSCAPE BEAUTIFICATION PLAZA	Tran	Contractor (Regular Award)	\$1,019,947	[Gantt bar for M1099]																								
1	M1100	Berenice Place (3933)	Siu	Contractor (Regular Award)	\$435,000	[Gantt bar for M1100]																								
1	M1137	AHSC Round 5 619 Westlake STI & TRA Improvements	Chen	Contractor (Regular Award)	\$3,047,583	[Gantt bar for M1137]																								
1	M1155	Bushwick Street Between Estara Ave and Ave 36	Lam	Contractor (Regular Award)	\$2,555,826	[Gantt bar for M1155]																								
2	M1041	Lankershim Boulevard Improvement Project	Lam	Contractor (Regular Award)	\$831,111	[Gantt bar for M1041]																								
2	M847	Magnolia Blvd (North) - Cahuenga Blvd to Vineland Ave	Lam	Contractor (Regular Award)	\$5,875,000	[Gantt bar for M847]																								
3	M1039	Sherman Way Great Street Improvement - Wilbur to Lindley	Cueva	Contractor (Regular Award)	\$2,599,110	[Gantt bar for M1039]																								
4	M1159	7260- 7280 and 7332 Pacific View Drive	Majidi	Contractor (Regular Award)	\$639,607	[Gantt bar for M1159]																								
4	M855	Ventura Blvd and Woodman Ave Improvements (Ventura-Cahuenga Specific Plan Funds)	Lam	Contractor (Regular Award)	\$1,099,700	[Gantt bar for M855]																								
4	M866	Ventura Bl Sidewalk Improvements (Cahuenga Specific Plan Fee Funded)	Lam	Design-Build	\$1,263,941	[Gantt bar for M866]																								
5	M1071	Mid-City Low Stress Bicycle Enhancement Corridor	Gebrewold	Contractor (Regular Award)	\$2,259,085	[Gantt bar for M1071]																								
5	M806	Exposition - West Bikeway - Northvale Segment	Haddadin	Contractor (Regular Award)	\$28,000,000	[Gantt bar for M806]																								
5	M987	National Blvd Sidewalk between Clarington and Jasmine	Siu	Contractor (Regular Award)	\$954,036	[Gantt bar for M987]																								
6	M1103	Ventura Canyon and Strathern Avenue	Majidi	Contractor (Regular Award)	\$875,100	[Gantt bar for M1103]																								
6	M1104	Victory Boulevard and Encino Ave Intersection	Gebrewold	Contractor (Regular Award)	\$150,000	[Gantt bar for M1104]																								
6	M1138	AHSC Round 5 619 Corazon Del Valle STI & TRA Improvements	Tran	Contractor (Regular Award)	\$5,640,007	[Gantt bar for M1138]																								
6	M1158	High Priority Sidewalk Gap Closures and Pedestrian Safety Improvements	Lam	Contractor (Regular Award)	\$1,650,000	[Gantt bar for M1158]																								
6	M1167	Active Transportation Cycle 5: SRTS Panorama City Elementary School Project	Abbound	Contractor (Regular Award)	\$6,149,000	[Gantt bar for M1167]																								
7	M571	Burbank Blvd & Woodley Ave Intersection Impr	Lam	Contractor (Regular Award)	\$393,370	[Gantt bar for M571]																								
7	M1091	Maclay Street Reconfiguration Project	Lam	Contractor (Regular Award)	\$1,700,000	[Gantt bar for M1091]																								
7	M1156	Foothill Blvd. (12061) and Pierce Street Tunnel	Huang	General Services Dept Forces	\$160,839	[Gantt bar for M1156]																								
7	M662	Harding St. Bridge Rock Slope Protection	Lam	Contractor (On-Call)	\$700,320	[Gantt bar for M662]																								
8	M1094	LANI West Blvd Community Linkages	Gebrewold	N/A - Design Project Only	\$1,059,745	[Gantt bar for M1094]																								
8	M1116	Western Gage Median Park Project	Masuda	Other (Explain in Project Description)	\$265,000	[Gantt bar for M1116]																								
8	M1154	Browning Blvd. (1700) Pedestrian Tunnel Closure	Huang	General Services Dept Forces	\$332,548	[Gantt bar for M1154]																								
8	M1172	67th Street Improvement Project	Haddadin	Contractor (Regular Award)	\$1,500,000	[Gantt bar for M1172]																								
8	M852	Slauson Ave. Street Improvements from Western to 5th Avenue	Gebrewold	Contractor (Regular Award)	\$3,562,936	[Gantt bar for M852]																								
8	M856	HSIP Cycle 7 Great St. Crenshaw Blvd Improvements - Florence and 79th Street	Lam	Contractor (Regular Award)	\$3,440,402	[Gantt bar for M856]																								
8	M926	Active Transportation Program Cycle 3: Jefferson Boulevard Complete Streets	Abbound	Contractor (Regular Award)	\$10,664,617	[Gantt bar for M926]																								
9	CS0006	Avalon Blvd Improvements, 56th St. and Manchester Ave (Complete Streets Program)	Medina	Contractor (Regular Award)	\$17,747,400	[Gantt bar for CS0006]																								
9	M1139	AHSC Round 5 619 Parkview STI & TRA Improvements	Tran	Contractor (Regular Award)	\$5,523,474	[Gantt bar for M1139]																								
9	M1166	Active Transportation Cycle 5: SRTS Carver Middle and Ascot Avenue and Harmony Elementary Schools Pr	Abbound	Contractor (Regular Award)	\$6,030,000	[Gantt bar for M1166]																								
9	M1171	41st Dr Street Improvement Project	Haddadin	Contractor (Regular Award)	\$1,500,000	[Gantt bar for M1171]																								
9	M830	ATP SRTS Menlo Ave ES & Vernon Ave. ES	Cueva	Contractor (Regular Award)	\$4,694,550	[Gantt bar for M830]																								
9	M831	ATP SRTS Dolores Huerta ES, 28th St ES, & Quincy Jones ES	Cueva	Contractor (Regular Award)	\$5,305,131	[Gantt bar for M831]																								
9	M870	Central Avenue Pedestrian Improvements	Abbound	Contractor (Regular Award)	\$6,454,738	[Gantt bar for M870]																								
9	M871	Central Avenue Streetscape	Abbound	Contractor (Regular Award)	\$1,520,896	[Gantt bar for M871]																								
9	M909	Gage Ave Public Safety Median Improvements - Avalon Blvd to Central Ave	Gebrewold	Contractor (Regular Award)	\$1,298,842	[Gantt bar for M909]																								
9	M927	SRTS 3 Menlo Ave Elementary School Pedestrian Improvements (DOT Proj)	Cueva	Contractor (Regular Award)	\$331,741	[Gantt bar for M927]																								
9	MVZ0006A	Avalon Blvd Improvements Segment 2, 56th St. to San Pedro St.	Medina	Not Specified	\$5,325,000	[Gantt bar for MVZ0006A]																								
10	M1009	Degnan Blvd Street Improvement Project	Medina	Contractor (Regular Award)	\$2,747,689	[Gantt bar for M1009]																								
10	M1069	Koreatown Gateway Project	Masuda	Design-Build	\$3,630,933	[Gantt bar for M1069]																								
10	M1073	Bicycle Friendly Streets (4th Street at New Hampshire)	Huang	Contractor (Regular Award)	\$422,985	[Gantt bar for M1073]																								
10	M1142	AHSC Round 5 619 Washington Arts Collective STI & TRA Improvements	Tran	Contractor (Regular Award)	\$1,853,449	[Gantt bar for M1142]																								
11	M1006	Sanborn Ave Reconstruction near Washington Bl Street Improvement	Carrillo	Contractor (Regular Award)	\$695,880	[Gantt bar for M1006]																								
11	M1014	Venice Beach Ocean Front Walk Crash-Ramps and Bollards	Gebrewold	Contractor (Regular Award)	\$3,166,600	[Gantt bar for M1014]																								
11	M1118	Great Streets Centinela Ave at Greene Ave	Siu	Street Services Forces	\$500,000	[Gantt bar for M1118]																								
11	M1124	Wade Street Reconfiguration Project	Lam	Contractor (Regular Award)	\$2,820,000	[Gantt bar for M1124]																								
11	M1141	AHSC Round 5 619 Thatcher Yard Housing STI & TRA Improvements	Tran	Contractor (Regular Award)	\$3,236,279	[Gantt bar for M1141]																								
11	M1160	Paseo Miramar (361-431 & 767)	Majidi	Contractor (Regular Award)	\$264,046	[Gantt bar for M1160]																								
12	M1015	Zelzah AVE. IMPROVEMENTS RIDGEWAY RD. TO NEWCASTLE AVE.	Abassy	Contractor (Regular Award)	\$11,019,523	[Gantt bar for M1015]																								
12	M286	San Fernando Road Widening at Balboa Road	Lam	Contractor (Regular Award)	\$2,451,648	[Gantt bar for M286]																								
12	M581	Balboa and San Fernando Intersection Improv	Lam	Contractor (Regular Award)	\$527,947	[Gantt bar for M581]																								
12	M896	Balboa Bl Widening at Devonshire Street	Tran	Contractor (Regular Award)	\$2,299,671	[Gantt bar for M896]																								
13	M1025	AHSC Round 3 - PATH Villas Hollywood STI and TRA Improvements	Tran	Contractor (Regular Award)	\$3,297,007	[Gantt bar for M1025]																								
13	M1043	Beverly (Juanita) and Madison Public Infrastructure Improvement	Medina	Contractor (Regular Award)	\$1,008,644	[Gantt bar for M1043]																								
13	M1078	AHSC Round 4 - Hollywood Arts Collective STI & TRA Improvements	Tran	Contractor (Regular Award)	\$2,797,656	[Gantt bar for M1078]																								
13	M1101	Fletcher Drive and La Ciede Ave	Gebrewold	Contractor (Regular Award)	\$2,582,109	[Gantt bar for M1101]																								
13	M1102	Montana Street at Allesandro Street Sidewalk Improvement	Siu	Contractor (Regular Award)	\$811,000	[Gantt bar for M1102]																								
13	M1143	AHSC Round 5 619 Santa Monica & Vermont STI & TRA Improvements	Tran	Contractor (Regular Award)	\$7,248,479	[Gantt bar for M1143]																								
13	M1144	Pedestrian Tunnel Closure at Logan Elementary School (Logan Street and Montana Street)	Huang	Contractor (Regular Award)	\$224,000	[Gantt bar for M1144]																								
13	M1145	Pedestrian Tunnel Closure at Rosemont Elementary School (Rosemont Avenue and Temple Street)	Huang	Contractor (Regular Award)	\$235,000	[Gantt bar for M1145]																								
13	M1157	Glendale Clinton Staircase	Gebrewold	Contractor (Regular Award)	\$1,014,000	[Gantt bar for M1157]																								
13	M1162	Safety Railing near 1780 Rotary Drive	Lam	Contractor (Regular Award)	\$75,000	[Gantt bar for M1162]																								
13	M1163	Wilcox (1718 N) Settlement Repair	Lam	Contractor (Regular Award)	\$196,861	[Gantt bar for M1163]																								
14	M1007	Via Marisol Street Reconstruction	Gebrewold	Contractor (Regular Award)	\$1,603,639	[Gantt bar for M1007]																								
14	M1082	AHSC Round 4 - Weingart Tower STI&TRA Improvements	Kim	Contractor (Regular Award)	\$8,311,326	[Gantt bar for M1082]																								
14	M1140	AHSC Round 5 619 Rose Hill Courts STI & TRA Improvements	Tran	Contractor (Regular Award)	\$6,320,649	[Gantt bar for M1140]																								
14	M1165	7th Street Streetscape Segment 3	Lam	Contractor (Regular Award)	\$7,079,722	[Gantt bar for M1165]																								
14	M326	Cesar Chavez Ave/Lorena St/Indiana St - Roundabout	Haddadin	Contractor (Regular Award)	\$6,146,000	[Gantt bar for M326]																								
14	M676	Olympic Blvd and Mateo Street Improvements	Tran	Contractor (Regular Award)	\$2,636,643	[Gantt bar for M676]																								
14	M833	ATP Little Tokyo Pedestrian Safety	Cueva	Contractor (Regular Award)	\$4,262,952	[Gantt bar for M833]																								
14	M835	ATP SRTS Sheridan ES & Breed St. ES	Cueva	Contractor (Regular Award)	\$4,999,161	[Gantt bar for M835]																								
14	M858	Broadway Historic Theater District Pedestrian Improvements - 4th St. to 6th St.	Bi	Contractor (Regular Award)	\$10,346,316	[Gantt bar for M858]																								
14	M864	HSIP 6 Olympic Blvd Between Lorena St and Soto St Pedestrian Crossing Safety Enhancements	Gebrewold	Contractor (Regular Award)	\$623,149	[Gantt bar for M864]																								
14	M886	Broadway Streetscape Implementation (8th-9th)	Bi	Contractor (Regular Award)	\$2,500,000	[Gantt bar for M886]																								
14	M887	Broadway Streetscape Implementation (1st-4th, 6th-8th, and 9th-12th Streets)	Bi	Contractor (Regular Award)	\$25,000,000	[Gantt bar for M887]																								
14	M915	7th Street Streetscape	Lam	Contractor (Regular Award)	\$6,271,931	[Gantt bar for M915]																								
14	X202A	ATP Cycle 2- Boyle Heights Pedestrian Linkage	Abbound	Contractor (Regular Award)	\$3,611,252	[Gantt bar for X202A]																								
14	X202B	ATP Cycle 3- Downtown Los Angeles Arts District Pedestrian and Cyclist Safety Project	Abbound	Contractor (Regular Award)	\$12,972,544	[Gantt bar for X202B]																								
15	m1067	ATP 4: 112th Street and Flournoy Elementary Schools Safety Improvements Project	Abbound	Contractor (Regular Award)	\$4,800,000	[Gantt bar for m1067]																								
15	M1076	Slater Ave Rail Grade Crossing Improvements	Abbound	N/A - Design Project Only	\$350,000	[Gantt bar for M1076]																								
15	M1079	AHSC Round 4 - Jordan Downs S3 STI & TRA Improvements	Tran	Contractor (Regular Award)	\$2,136,588	[Gantt bar for M1079]																								
15	M1096	South Bay MSP Crossing Upgrades	Haddadin	N/A - Design Project Only	\$2,415,126	[Gantt bar for M1096]																								
15	M1112	Connecting San Pedro Pedestrian Improvements and Multimodal Access	Abbound	Contractor (Regular Award)	\$9,022,704	[Gantt bar for M1112]																								
15	M660	Century Blvd Extension / Grape St to Alameda St.	Lam	Contractor (Regular Award)	\$13,562,123	[Gantt bar for M660]																								

Project: Master Schedule (UPRS)  
Date: Fri 5/26/23

Task		PreDesign		Cons		External Milestone		Inactive Milestone		Manual Task		Manual Summary		External Tasks		External Milestone
Split		Design		PostCons		Deadline		Inactive Milestone		Duration-only		Start-only		External Milestone		External Milestone
Milestone		BidAward		Crossing Safety		RightOfWay		Inactive Summary		Manual Summary Rollup		Finish-only		Progress		External Milestone

CD	CIP #s	Project Title	PM	Construction Vehicle	Const Cost	Street Improvement		
						2022	2023	2024
15	M717	Alameda St. Widening from Anaheim St. to PCH (North)	Huang	Contractor (Regular Award)	\$35,000,000	[Gantt bar: 2022-01-01 to 2023-06-30]		
15	M750	Alameda St. Widening from Harry Bridges to Anaheim (South)	Huang	Contractor (Regular Award)	\$42,000,000	[Gantt bar: 2022-01-01 to 2023-06-30]		
15	M851	Anaheim Street Widening from Farragut Ave. to Dominguez Channel	Haddadin	Contractor (Regular Award)	\$5,400,000	[Gantt bar: 2022-01-01 to 2023-06-30]		
1, 2, 4, 6, 8, 9, 11, 13, 14, 15, VR	M891	HSIP 7 RRFB Ramps and Median Islands - 28 locations	Lam	Contractor (Regular Award)	\$6,500,385	[Gantt bar: 2022-01-01 to 2023-06-30]		
1, 10	M859	Community Development Block Grant: Council District 1 Pedestrian Improvements Phase 1	Abboud	Contractor (Regular Award)	\$913,144	[Gantt bar: 2022-01-01 to 2023-06-30]		
2, 4	M1072	Chandler Cycletrack Gap Closure	Lam	Contractor (Regular Award)	\$4,257,602	[Gantt bar: 2022-01-01 to 2023-06-30]		
2, 8, 9, 10, 11, VR	M892	HSIP 7 Left Turn Phasing - 17 locations citywide	Lam	Contractor (Regular Award)	\$4,845,041	[Gantt bar: 2022-01-01 to 2023-06-30]		
3, 15	M904	Bridge Preventative Maintenance for Tampa Av, Peterson Av and Vermont Av	Masuda	Contractor (Regular Award)	\$154,879	[Gantt bar: 2022-01-01 to 2023-06-30]		
4, 6	M575	Burbank Blvd & Hayvenhurst Ave Intersection Impr	Lam	Contractor (Regular Award)	\$574,386	[Gantt bar: 2022-01-01 to 2023-06-30]		
5, 7, 9, 14	M868	ATP Cycle 2 - Pedestrian and Bicycle Neighborhood Intersection Enhancements	Bi	Contractor (Regular Award)	\$1,682,969	[Gantt bar: 2022-01-01 to 2023-06-30]		
8, 9	M1153	Vision Zero Fiscal Year 22/23	Carrillo	Street Services Forces	\$1,240,875	[Gantt bar: 2022-01-01 to 2023-06-30]		
8, 9	M905	I-110 Grand Av - Flower Av Revitalization, ExpressLanes Toll Grant Project	Medina	Street Services Forces	\$1,204,816	[Gantt bar: 2022-01-01 to 2023-06-30]		
8, 9, 15	MVZ0006B	Avalon Blvd Improvements Segment 3, Manchester Ave to 120th St.	Medina	Not Specified	\$6,720,000	[Gantt bar: 2022-01-01 to 2023-06-30]		
10, 13	m1068	ATP 4: Alexandria Avenue ES Neighborhood Safety IMPR Project (Local Funds)	Abboud	Contractor (Regular Award)	\$5,600,000	[Gantt bar: 2022-01-01 to 2023-06-30]		

Project: Master Schedule (UPRS)  
Date: Fri 5/26/23

Task	PreDesign	Cons	External Milestone	Inactive Milestone	Manual Task	Manual Summary	External Tasks	External Milestone	External Milestone
Split	Design	PostCons	Deadline	Inactive Milestone	Duration-only	Start-only	External Milestone	External Milestone	
Milestone	BidAward	RightOfWay	Inactive Task	Inactive Summary	Manual Summary Rollup	Finish-only	Progress	External Milestone	
